



# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #473614

**Service Request:** 473614  
**Department:** Public Works  
**Status:** CLOSED  
**Priority:** NORMAL  
**Created at:** March 04, 2020 12:00PM

**Requester:** Jose Vasquez  
**Home Phone:**  
**Work Phone:**  
**Other Phone:**  
**Created by:** josev

**Request:** PREVENTIVE MAINTENANCE. Assigned to Yanie (Siemens Tech).

**Location:** HARBOR BLVD / TRASK AVE,

**Public Property:** YES  
**Square Feet:**

**Eng. Permit:**  
**Police Num.:**  
**Fire Num.:**

**Total cost:** \$26.10

---

## Task #1

**Status:** CLOSED on March 04, 2020 01:00PM by Jose Vasquez

**Description:** No task description

**Comments:** VACUUMED CONTROLLER CABINET-REPLACED AIR FILTER-PERFORMED P.M. SCHEDULE-WALKED INTERSECTION-REMOVED GRAFFITI FROM CONTROLLER CABINET AND POLES.

**Category:** 700 SIGNAL MAINTENANCE (AUTO- **Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES

**Requester contacted:**

**Completed by:** Jose Vasquez

**ECD:**

**Total task cost:** \$26.097

**Actions:** 700.26 OTHER (SEE COMMENTS), 740.1 GRAFFITI REMOVED/COVERED

### Labor Costs

Name	Reg	OT	Total
Jose Vasquez	0.3 hours	0 hours	\$26.10
TOTAL	0.3 hours	0 hours	\$26.10



## GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #472877

**Service Request:** 472877

**Department:** Public Works

**Status:** CLOSED

**Priority:** HIGH

**Created at:** February 26, 2020 08:23AM

**Requester:** Dai Vu

**Home Phone:**

**Work Phone:**

**Other Phone:**

**Created by:** josev

**Request:** Pickup RedFlex camera out of traffic lanes so that PD can open up traffic flow.

**Location:** HARBOR BLVD / TRASK AVE, Police Activity

**Public Property:** YES

**Square Feet:**

**Eng. Permit:**

**Police Num.:**

**Fire Num.:**

**Total cost:** \$237.46

---

### Task #1

**Status:** CLOSED on February 26, 2020 09:45AM by Jose Vasquez

**Description:** No task description

**Comments:** Shan and I arrived and found the RedFlex pole and camera housing already resting on the median out of vehicle traffic. I spoke with a police officer and we decided to remove all of the "valuable" equipment from inside the damaged camera housing for safe keeping (per RedFlex) since the housing door was damaged and not able to be shut closed. Shan and I placed all of the pieces removed in a cardboard box delivered it to City Hall (Engineering TMC). WE placed the Flash device in a location at the back of the yard till somebody from RedFlex can come pick it up. We notified the officer and Dai of where we had placed the equipment.

**Category:** 800 MISC.

**Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES

**Requester contacted:**

**Completed by:** Jose Vasquez

**ECD:**

**Total task cost:** \$237.465

**Actions:** 800.1 COMPLETE

#### Labor Costs

Name	Reg	OT	Total
Shan Lewis	1.5 hours	0 hours	\$106.98
Jose Vasquez	1.5 hours	0 hours	\$130.48
TOTAL	3.0 hours	0 hours	\$237.46



# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #458073

**Service Request:** 458073

**Department:** Public Works

**Status:** CLOSED

**Priority:** NORMAL

**Created at:** June 07, 2019 02:25AM

**Requester:** Signal Maintenance

**Home Phone:**

**Work Phone:**

**Other Phone:**

**Created by:** shanl

**Request:** REMOVE EXISTING CONFLICT MONITOR & INSTALL TESTED MONITOR.

**Location:** HARBOR BLVD / TRASK AVE,

**Public Property:** YES

**Square Feet:**

**Eng. Permit:**

**Police Num.:**

**Fire Num.:**

**Total cost:** \$12.91

---

## Task #1

**Status:** CLOSED on June 07, 2019 02:35AM by Shan Lewis

**Description:** REMOVE EXISTING CONFLICT MONITOR & INSTALL TESTED MONITOR.

**Comments:** REMOVED CONFLICT MONITOR & INSTALLED TESTED MONITOR #091205128

**Category:** 700 SIGNAL MAINTENANCE (AUTO- **Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES

**Requester contacted:**

**Completed by:** Shan Lewis

**ECD:**

**Total task cost:** \$12.912

**Actions:** 700.26 OTHER (SEE COMMENTS)

### Labor Costs

Name	Reg	OT	Total
Shan Lewis	0.2 hours	0 hours	\$12.91
TOTAL	0.2 hours	0 hours	\$12.91



# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #457380

**Service Request:** 457380

**Department:** Public Works

**Status:** CLOSED

**Priority:** NORMAL

**Created at:** May 22, 2019 06:00AM

**Requester:** Signal Maintenance

**Home Phone:**

**Work Phone:**

**Other Phone:**

**Created by:** shanl

**Request:** "USA" DIG ALERT, MARK UNDERGROUND UTILITIES.

**Location:** HARBOR BLVD / TRASK AVE,

**Public Property:** YES

**Square Feet:**

**Eng. Permit:**

**Police Num.:**

**Fire Num.:**

**Total cost:** \$71.66

---

## Task #1

**Status:** CLOSED on May 22, 2019 06:30AM by Shan Lewis

**Description:** "USA" DIG ALERT, MARK UNDERGROUND UTILITIES.

**Comments:** MARKED TRAFFIC SIGNAL UNDERGROUND UTILITIES AND FIBER.

**Category:** 700 SIGNAL MAINTENANCE (AUTO- **Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES

**Requester contacted:**

**Completed by:** Shan Lewis

**ECD:**

**Total task cost:** \$71.655

**Actions:** 700.26 OTHER (SEE COMMENTS)

### Labor Costs

Name	Reg	OT	Total
Shan Lewis	0.5 hours	0 hours	\$32.28
Jose Vasquez	0.5 hours	0 hours	\$39.38
TOTAL	1.0 hours	0 hours	\$71.66



# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #454066

**Service Request:** 454066  
**Department:** Public Works  
**Status:** CLOSED  
**Priority:** NORMAL  
**Created at:** March 19, 2019 07:55AM

**Requester:** Signal Maintenance  
**Home Phone:**  
**Work Phone:**  
**Other Phone:**  
**Created by:** shanl

**Request:** S/B HARBOR, 1ST W/P ON THE RIGHT IS POPPING OFF & ON  
**Location:** HARBOR BLVD / TRASK AVE,

**Public Property:** YES  
**Square Feet:**

**Eng. Permit:**  
**Police Num.:**  
**Fire Num.:**

**Total cost:** \$12.91

## Task #1

**Status:** CLOSED on March 19, 2019 08:05AM by Shan Lewis  
**Description:** S/B HARBOR, 1ST W/P ON THE RIGHT IS POPPING OFF & ON  
**Comments:** INSTALLED A NEW LAMP.  
**Category:** 700 SIGNAL MAINTENANCE (AUTO- **Assigned to:** Jose Vasquez  
**Division:** ENGR SERVICES **Requester contacted:**  
**Completed by:** Shan Lewis **ECD:**  
**Total task cost:** \$12.912  
**Actions:** 700.1 REPLACED OLD LAMP WITH NEW LED MODULE

### Labor Costs

Name	Reg	OT	Total
Shan Lewis	0.2 hours	0 hours	\$12.91
TOTAL	0.2 hours	0 hours	\$12.91



# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #454063

**Service Request:** 454063  
**Department:** Public Works  
**Status:** CLOSED  
**Priority:** NORMAL  
**Created at:** March 19, 2019 07:40AM

**Requester:** Signal Maintenance  
**Home Phone:**  
**Work Phone:**  
**Other Phone:**  
**Created by:** shanl

**Request:** E/B TRASK, FIRST W/P ON THE RIGHT IS POPPING ON & OFF.  
**Location:** HARBOR BLVD / TRASK AVE, CLINTON SCHOOL CROSSING

**Public Property:** YES  
**Square Feet:**

**Eng. Permit:**  
**Police Num.:**  
**Fire Num.:**

**Total cost:** \$12.91

## Task #1

**Status:** CLOSED on March 19, 2019 08:00AM by Shan Lewis  
**Description:** E/B TRASK, FIRST W/P ON THE RIGHT IS POPPING ON & OFF.  
**Comments:** INSTALLED A NEW LAMP.  
**Category:** 700 SIGNAL MAINTENANCE (AUTO- **Assigned to:** Jose Vasquez  
**Division:** ENGR SERVICES **Requester contacted:**  
**Completed by:** Shan Lewis **ECD:**  
**Total task cost:** \$12.912  
**Actions:** 700.1 REPLACED OLD LAMP WITH NEW LED MODULE

### Labor Costs

Name	Reg	OT	Total
Shan Lewis	0.2 hours	0 hours	\$12.91
TOTAL	0.2 hours	0 hours	\$12.91



# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #451425

**Service Request:** 451425  
**Department:** Public Works  
**Status:** CLOSED  
**Priority:** NORMAL  
**Created at:** January 28, 2019 07:00AM

**Requester:** Signal Maintenance  
**Home Phone:**  
**Work Phone:**  
**Other Phone:**  
**Created by:** shanl

**Request:** PREVENTIVE MAINTENANCE.

**Location:** HARBOR BLVD / TRASK AVE,

**Public Property:** NO  
**Square Feet:**

**Eng. Permit:**  
**Police Num.:**  
**Fire Num.:**

**Total cost:** \$214.97

---

## Task #1

**Status:** CLOSED on January 28, 2019 08:30AM by Shan Lewis

**Description:** PREVENTIVE MAINTENANCE.

**Comments:** VACUUMED CONTROLLER CABINET-REPLACED AIR FILTER-PERFORMED P.M. SCHEDULE-WALKED INTERSECTION-REMOVED GRAFFITI FROM CONTROLLER CABINET AND POLES.

**Category:** 700 SIGNAL MAINTENANCE (AUTO- **Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES

**Requester contacted:**

**Completed by:** Shan Lewis

**ECD:**

**Total task cost:** \$214.965

**Actions:** 700.26 OTHER (SEE COMMENTS), 740.1 GRAFFITI REMOVED/COVERED

### Labor Costs

Name	Reg	OT	Total
Shan Lewis	1.5 hours	0 hours	\$96.84
Jose Vasquez	1.5 hours	0 hours	\$118.12
TOTAL	3.0 hours	0 hours	\$214.97



# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #449895

**Service Request:** 449895

**Department:** Public Works

**Status:** CLOSED

**Priority:** NORMAL

**Created at:** December 13, 2018 05:45AM

**Requester:** Signal Maintenance

**Home Phone:**

**Work Phone:**

**Other Phone:**

**Created by:** shanl

**Request:** INSTALLED LOCK TO SECURE SERVICE.

**Location:** HARBOR BLVD / TRASK AVE, 22 UNDERPASS LIGHTING

**Public Property:** NO

**Square Feet:**

**Eng. Permit:**

**Police Num.:**

**Fire Num.:**

**Total cost:** \$28.66

---

## Task #1

**Status:** CLOSED on December 13, 2018 06:00AM by Shan Lewis

**Description:** INSTALLED LOCK TO SECURE SERVICE.

**Comments:** INSTALLED A CITY LOCK ON SERVICE.

**Category:** 700 SIGNAL MAINTENANCE (AUTO- **Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES

**Requester contacted:**

**Completed by:** Jose Vasquez

**ECD:**

**Total task cost:** \$28.662

**Actions:** 700.26 OTHER (SEE COMMENTS)

### Labor Costs

Name	Reg	OT	Total
Shan Lewis	0.2 hours	0 hours	\$12.91
Jose Vasquez	0.2 hours	0 hours	\$15.75
TOTAL	0.4 hours	0 hours	\$28.66





# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #449565

**Service Request:** 449565

**Department:** Public Works

**Status:** CLOSED

**Priority:** NORMAL

**Created at:** December 12, 2018 12:00PM

**Request:** 7TH WP GOING W/B IS OUT

**Location:** HARBOR BLVD / TRASK AVE,

**Public Property:** NO

**Square Feet:**

**Total cost:** \$143.31

**Requester:** Signal Maintenance

**Home Phone:**

**Work Phone:**

**Other Phone:**

**Created by:** shanl

**Eng. Permit:**

**Police Num.:**

**Fire Num.:**

---

## Task #1

**Status:** CLOSED on December 12, 2018 01:00PM by Shan Lewis

**Description:** 7TH WP GOING W/B IS OUT

**Comments:** INSTALLED A NEW LAMP & BALLAST

**Category:** 710 ST. LIGHTS/ILLUM. NAME SIGNS **Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES

**Requester contacted:**

**Completed by:** Shan Lewis

**ECD:**

**Total task cost:** \$143.31

**Actions:** 710.1 REPLACED LAMP, 710.5 INSTALLED NEW LED LIGHT FIXTURE

### Labor Costs

Name	Reg	OT	Total
Shan Lewis	1.0 hours	0 hours	\$64.56
Jose Vasquez	1.0 hours	0 hours	\$78.75
TOTAL	2.0 hours	0 hours	\$143.31



# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #447610

**Service Request:** 447610

**Department:** Public Works

**Status:** CLOSED

**Priority:** NORMAL

**Created at:** October 25, 2018 09:30AM

**Requester:** Jose Vasquez

**Home Phone:**

**Work Phone:**

**Other Phone:**

**Created by:** josev

**Request:** 3rd and 6th WP going EB are out. 3rd WP going WB is out.

**Location:** HARBOR BLVD / TRASK AVE, 22 frwy underpass lights.

**Public Property:** NO

**Square Feet:**

**Eng. Permit:**

**Police Num.:**

**Fire Num.:**

**Total cost:** \$30.75

---

## Task #1

**Status:** CLOSED on October 25, 2018 10:00AM by Jose Vasquez

**Description:** No task description

**Category:** 710 ST. LIGHTS/ILLUM. NAME SIGNS **Assigned to:** Shan Lewis

**Division:** ENGR SERVICES **Requester contacted:**

**Completed by:** Shan Lewis **ECD:**

**Total task cost:** \$30.745

**Actions:** 710.1 REPLACED LAMP

### Labor Costs

Name	Reg	OT	Total
Shan Lewis	0.5 hours	0 hours	\$30.75
TOTAL	0.5 hours	0 hours	\$30.75



# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #446386

**Service Request:** 446386  
**Department:** Public Works  
**Status:** CLOSED  
**Priority:** NORMAL  
**Created at:** September 26, 2018 10:30AM

**Requester:** Signal Maintenance  
**Home Phone:**  
**Work Phone:**  
**Other Phone:**  
**Created by:** shanl

**Request:** N/B TO W/B OVERHEAD RED ARROW IS OUT.

**Location:** HARBOR BLVD / TRASK AVE,

**Public Property:** NO  
**Square Feet:**

**Eng. Permit:**  
**Police Num.:**  
**Fire Num.:**

**Total cost:** \$140.24

---

## Task #1

**Status:** CLOSED on September 26, 2018 11:30AM by Shan Lewis

**Description:** N/B TO W/B OVERHEAD RED ARROW IS OUT.

**Comments:** CALLED OUT SIEMENS TO INSTALL A CITY PROVIDED 12" RED ARROW LED MODULE. OUR AERIAL TRUCK (597) IS AT ALTEC FOR REPAIRS.

**Category:** 700 SIGNAL MAINTENANCE (AUTO- **Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES

**Requester contacted:**

**Completed by:** Shan Lewis

**ECD:**

**Total task cost:** \$140.24

**Actions:** 700.26 OTHER (SEE COMMENTS)

### Labor Costs

Name	Reg	OT	Total
Jose Vasquez	1.0 hours	0 hours	\$78.75
Shan Lewis	1.0 hours	0 hours	\$61.49
TOTAL	2.0 hours	0 hours	\$140.24



# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #442304

**Service Request:** 442304

**Department:** Public Works

**Status:** CLOSED

**Priority:** NORMAL

**Created at:** June 29, 2018 02:00AM

**Requester:** Jose Vasquez

**Home Phone:**

**Work Phone:**

**Other Phone:**

**Created by:** josev

**Request:** REMOVE EXISTING CONFLICT MONITOR & INSTALL TESTED MONITOR. Install new SDLC cables if needed.

**Location:** HARBOR BLVD / TRASK AVE,

**Public Property:** NO

**Square Feet:**

**Eng. Permit:**

**Police Num.:**

**Fire Num.:**

**Total cost:** \$40.99

---

## Task #1

**Status:** CLOSED on June 29, 2018 02:15AM by Jose Vasquez

**Description:** No task description

**Comments:** REMOVED CONFLICT MONITOR & INSTALLED TESTED MONITOR #160701374. Installed new cabinet SDLC cables.

**Category:** 700 SIGNAL MAINTENANCE (AUTO- **Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES

**Requester contacted:**

**Completed by:** Jose Vasquez

**ECD:**

**Total task cost:** \$40.995

**Actions:** 700.26 OTHER (SEE COMMENTS)

### Labor Costs

Name	Reg	OT	Total
Jose Vasquez	0.3 hours	0 hours	\$23.02
Shan Lewis	0.3 hours	0 hours	\$17.97
TOTAL	0.6 hours	0 hours	\$40.99



## GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #440562

**Service Request:** 440562

**Department:**

**Status:** CLOSED

**Priority:** NORMAL

**Created at:** May 10, 2018 10:45AM

**Requester:** Signal Maintenance

**Home Phone:**

**Work Phone:**

**Other Phone:**

**Created by:** shanl

**Request:** 1ST & 5TH WALL PACK ON THE RIGHT GOING S/B ON HARBOR ARE OUT.

**Location:** HARBOR BLVD / TRASK AVE, 22 UNDERPASS

**Public Property:** NO

**Square Feet:**

**Eng. Permit:**

**Police Num.:**

**Fire Num.:**

**Total cost:** \$29.95

---

### Task #1

**Status:** CLOSED on May 10, 2018 11:15AM by Shan Lewis

**Description:** 1ST & 5TH WALL PACK ON THE RIGHT GOING S/B ON HARBOR ARE OUT.

**Comments:** INSTALLED NEW LAMPS.

**Category:** 710 ST. LIGHTS/ILLUM. NAME SIGNS **Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES **Requester contacted:**

**Completed by:** Shan Lewis **ECD:**

**Total task cost:** \$29.955

**Actions:** 710.1 REPLACED LAMP

#### Labor Costs

Name	Reg	OT	Total
Shan Lewis	0.5 hours	0 hours	\$29.95
TOTAL	0.5 hours	0 hours	\$29.95



# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #440499

**Service Request:** 440499

**Department:** Public Works

**Status:** CLOSED

**Priority:** NORMAL

**Created at:** May 10, 2018 10:30AM

**Requester:** Signal Maintenance

**Home Phone:**

**Work Phone:**

**Other Phone:**

**Created by:** shanl

**Request:** 10TH WALL PACK GOING E/B ON TRASK IS OUT.

**Location:** HARBOR BLVD / TRASK AVE, 22 UNDERPASS

**Public Property:** NO

**Square Feet:**

**Eng. Permit:**

**Police Num.:**

**Fire Num.:**

**Total cost:** \$11.98

---

## Task #1

**Status:** CLOSED on May 10, 2018 10:45AM by Shan Lewis

**Description:** 10TH WALL PACK GOING E/B ON TRASK IS OUT.

**Comments:** INSTALLED A NEW LAMP.

**Category:** 710 ST. LIGHTS/ILLUM. NAME SIGNS **Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES

**Requester contacted:**

**Completed by:** Shan Lewis

**ECD:**

**Total task cost:** \$11.982

**Actions:** 710.1 REPLACED LAMP

### Labor Costs

Name	Reg	OT	Total
Shan Lewis	0.2 hours	0 hours	\$11.98
TOTAL	0.2 hours	0 hours	\$11.98



# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #439467

**Service Request:** 439467  
**Department:** Public Works  
**Status:** CLOSED  
**Priority:** NORMAL  
**Created at:** April 20, 2018 07:30AM

**Requester:** Signal Maintenance  
**Home Phone:**  
**Work Phone:**  
**Other Phone:**  
**Created by:** shanl

**Request:** "USA" DIG ALERT, MARK UNDERGROUND UTILITIES.

**Location:** HARBOR BLVD / TRASK AVE,

**Public Property:** NO  
**Square Feet:**

**Eng. Permit:**  
**Police Num.:**  
**Fire Num.:**

**Total cost:** \$199.49

---

## Task #1

**Status:** CLOSED on April 20, 2018 09:00PM by Shan Lewis

**Description:** "USA" DIG ALERT, MARK UNDERGROUND UTILITIES.

**Comments:** MARKED TRAFFIC SIGNAL UNDERGROUND UTILITIES AND FIBER.

**Category:** 700 SIGNAL MAINTENANCE (AUTO- **Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES **Requester contacted:**

**Completed by:** Shan Lewis **ECD:**

**Total task cost:** \$199.485

**Actions:** 700.20 REMOVED PEDESTRIAN RECALL/S

### Labor Costs

Name	Reg	OT	Total
Shan Lewis	1.5 hours	0 hours	\$89.86
Jose Vasquez	1.5 hours	0 hours	\$109.62
TOTAL	3.0 hours	0 hours	\$199.49



# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #439247

**Service Request:** 439247

**Department:** Police

**Status:** CLOSED

**Priority:** EMERGENCY

**Created at:** April 17, 2018 01:35AM

**Requester:** GG Dispatch

**Home Phone:**

**Work Phone:**

**Other Phone:**

**Created by:** josev

**Request:** T/C, 10 ft. signal pole knocked down on the NEC.

**Location:** HARBOR BLVD / TRASK AVE,

**Public Property:** NO

**Square Feet:**

**Eng. Permit:**

**Police Num.:** 18021845

**Fire Num.:**

**Total cost:** \$2906.43

**File attachments:** 10

**Task #1**

**Status:** CLOSED on April 17, 2018 03:00PM by Jose Vasquez

**Description:** No task description

**Comments:** The entire 10 ft. 1-D pole and signal equipment was destroyed on the NEC. Shan and I installed a new 1-D pole, a complete pedestrian push button station. Siemens came out and installed a TV-2-T, 3 Sec 12"RYG Signal head (loaded) and a 5 Sec 12"RYGYG Signal head (loaded).

**Category:** 700 SIGNAL MAINTENANCE (AUTO-

**Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES

**Requester contacted:**

**Completed by:** Jose Vasquez

**ECD:**

**Total task cost:** \$2906.43

**Actions:** 700.14 REPLACED PED P/BUTTON FRAMEWORK, 700.26 OTHER (SEE COMMENTS)

**Labor Costs**




Name	Reg	OT	Total
Shan Lewis	3.0 hours	4.5 hours	\$419.36
Jose Vasquez	3.0 hours	4.5 hours	\$511.52
<b>TOTAL</b>	6.0 hours	9.0 hours	\$930.87

**Equipment/Material Costs**

Num	Description	Cost
1	UNIT 788 - 07 FORD F550 SIGN TRK	\$543.66
2	VEH 586 - CHEVY UTIL TRUCK	\$331.80
3	10 ft. 1D pole	\$533.00
4	4.5 x 7.134 Rectagle hand-hole cover	\$31.32
5	Right arrow pedestrian plaque	\$25.00
6	TV-2-T Bronze Green framework Only	\$336.18
7	Pedestrian push-button	\$45.00
8	Pedestrian frame work	\$129.60
	<b>TOTAL</b>	<b>\$1975.56</b>



Photos for Workorder #439247

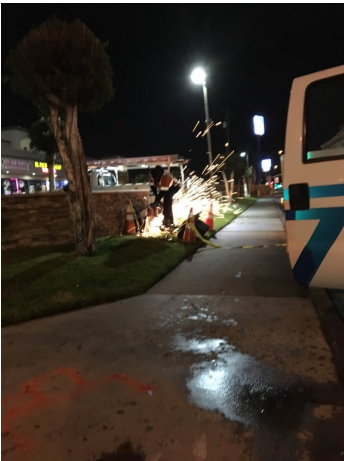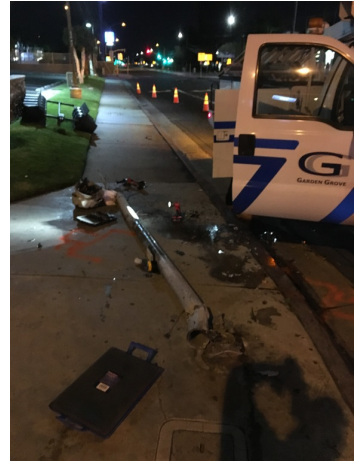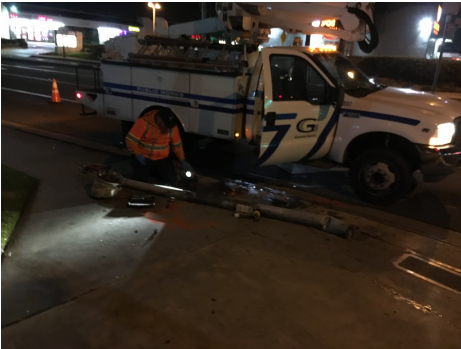



Photos for Workorder #439247



# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #437145

**Service Request:** 437145

**Department:** Police

**Status:** CLOSED

**Priority:** HIGH

**Created at:** February 23, 2018 11:00AM

**Requester:** PD Dispatch

**Home Phone:**

**Work Phone:**

**Other Phone:**

**Created by:** josev

**Request:** SB left turn is not changing or is too short.

**Location:** HARBOR BLVD / TRASK AVE,

**Public Property:** NO

**Square Feet:**

**Eng. Permit:**

**Police Num.:**

**Fire Num.:**

**Total cost:** \$132.99

---

## Task #1

**Status:** CLOSED on February 23, 2018 12:00PM by Jose Vasquez

**Description:** No task description

**Comments:** Shan and I arrived and we watched the intersection for several cycles. We found that all detection was working properly. I added extra detectors to the phase 7 detector file and placed phase 7 on Red Lock Detect just incase.

**Category:** 700 SIGNAL MAINTENANCE (AUTO- **Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES

**Requester contacted:**

**Completed by:** Jose Vasquez

**ECD:**

**Total task cost:** \$132.99

**Actions:** 700.26 OTHER (SEE COMMENTS), 700.22 RETUNED DETECTOR / DETECTOR ZONE

### Labor Costs

Name	Reg	OT	Total
Jose Vasquez	1.0 hours	0 hours	\$73.08
Shan Lewis	1.0 hours	0 hours	\$59.91
TOTAL	2.0 hours	0 hours	\$132.99



# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #436773

**Service Request:** 436773  
**Department:** Public Works  
**Status:** CLOSED  
**Priority:** NORMAL  
**Created at:** February 12, 2018 09:00AM

**Requester:** Signal Maintenance  
**Home Phone:**  
**Work Phone:**  
**Other Phone:**  
**Created by:** shanl

**Request:** PREVENTIVE MAINTENANCE.  
**Location:** HARBOR BLVD / TRASK AVE,

**Public Property:** NO  
**Square Feet:**

**Eng. Permit:**  
**Police Num.:**  
**Fire Num.:**

**Total cost:** \$199.49

## Task #1

**Status:** CLOSED on February 12, 2018 10:30AM by Shan Lewis

**Description:** PREVENTIVE MAINTENANCE.

**Comments:** VACUUMED CONTROLLER CABINET-REPLACED AIR FILTER-PERFORMED P.M. SCHEDULE-WALKED INTERSECTION-REMOVED GRAFFITI FROM CONTROLLER CABINET AND POLES. WE FOUND THAT THE N/B 12" OVERHEAD RED WAS OUT. JOSE REPLACED IT WITH NEW 12" RED LED MODULE. THE SEC GOING NORTH PUSH BUTTON WAS MOUNTED WITH ONLY ONE BOLT BY A CONTRACTOR. JOSE TAPPED A NEW HOLE AND REMOUNTED THE PUSH BUTTON ASSEMBLY, USING BOTH OF THE REQUIRED MOUNTING POINTS. WE ALSO REPLACED A BROKEN PULL BOX LID ON THE NEC OF TRASK & HARBOR.

**Category:** 700 SIGNAL MAINTENANCE (AUTO- **Assigned to:** Jose Vasquez  
**Division:** ENGR SERVICES **Requester contacted:**  
**Completed by:** Jose Vasquez **ECD:**

**Total task cost:** \$199.485

**Actions:** 700.1 REPLACED OLD LAMP WITH NEW LED MODULE, 700.20 REMOVED PEDESTRIAN RECALL/S, 740.1 GRAFFITI REMOVED/COVERED

### Labor Costs

Name	Reg	OT	Total
Shan Lewis	1.5 hours	0 hours	\$89.86
Jose Vasquez	1.5 hours	0 hours	\$109.62
<b>TOTAL</b>	<b>3.0 hours</b>	<b>0 hours</b>	<b>\$199.49</b>



# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #436604

**Service Request:** 436604  
**Department:** Public Works  
**Status:** CLOSED  
**Priority:** NORMAL  
**Created at:** February 07, 2018 02:45PM

**Requester:** Jose Vasquez  
**Home Phone:**  
**Work Phone:**  
**Other Phone:**  
**Created by:** josev

**Request:** Hand hole cover for the mast-arm pole on the NEC is laying next to the pole.  
**Location:** HARBOR BLVD / TRASK AVE,

**Public Property:** NO  
**Square Feet:**

**Eng. Permit:**  
**Police Num.:**  
**Fire Num.:**

**Total cost:** \$17.97

---

## Task #1

**Status:** CLOSED on February 07, 2018 03:00PM by Jose Vasquez

**Description:** No task description

**Comments:** Shan reinstalled the hand-hole cover.

**Category:** 700 SIGNAL MAINTENANCE (AUTO-

**Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES

**Requester contacted:**

**Completed by:** Jose Vasquez

**ECD:**

**Total task cost:** \$17.973

**Actions:** 700.26 OTHER (SEE COMMENTS)

### Labor Costs

Name	Reg	OT	Total
Shan Lewis	0.3 hours	0 hours	\$17.97
TOTAL	0.3 hours	0 hours	\$17.97



# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #435255

**Service Request:** 435255

**Department:** Public Works

**Status:** CLOSED

**Priority:** NORMAL

**Created at:** December 05, 2017 09:28AM

**Requester:** Signal Maintenance

**Home Phone:**

**Work Phone:**

**Other Phone:**

**Created by:** shanl

**Request:** 3rd wall pack on the right heading Northbound on Harbor is out

**Location:** HARBOR BLVD / TRASK AVE, 22 Underpass

**Public Property:** NO

**Square Feet:**

**Eng. Permit:**

**Police Num.:**

**Fire Num.:**

**Total cost:** \$26.60

---

## Task #1

**Status:** CLOSED on December 05, 2017 09:40AM by Shan Lewis

**Description:** 3rd wall pack on the right heading Northbound on Harbor is out

**Comments:** Installed a new lamp.

**Category:** 710 ST. LIGHTS/ILLUM. NAME SIGNS **Assigned to:**

**Division:** ENGR SERVICES **Requester contacted:**

**Completed by:** Shan Lewis **ECD:**

**Total task cost:** \$26.598

**Actions:** 710.1 REPLACED LAMP

### Labor Costs

Name	Reg	OT	Total
Jose Vasquez	0.2 hours	0 hours	\$14.62
Shan Lewis	0.2 hours	0 hours	\$11.98
TOTAL	0.4 hours	0 hours	\$26.60



# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #435191

**Service Request:** 435191

**Department:** Public Works

**Status:** CLOSED

**Priority:** NORMAL

**Created at:** December 05, 2017 08:45AM

**Requester:** Signal Maintenance

**Home Phone:**

**Work Phone:**

**Other Phone:**

**Created by:** shanl

**Request:** The 6th wall pack on the right side going Westbound on Trask is out.

**Location:** HARBOR BLVD / TRASK AVE, 22 Underpass

**Public Property:** NO

**Square Feet:**

**Eng. Permit:**

**Police Num.:**

**Fire Num.:**

**Total cost:** \$26.60

---

## Task #1

**Status:** CLOSED on December 05, 2017 09:00AM by Shan Lewis

**Description:** The 6th wall pack on the right side going Westbound on Trask is out.

**Comments:** Installed a new lamp.

**Category:** 710 ST. LIGHTS/ILLUM. NAME SIGNS **Assigned to:**

**Division:** ENGR SERVICES **Requester contacted:**

**Completed by:** Shan Lewis **ECD:**

**Total task cost:** \$26.598

**Actions:** 710.1 REPLACED LAMP

### Labor Costs

Name	Reg	OT	Total
Jose Vasquez	0.2 hours	0 hours	\$14.62
Shan Lewis	0.2 hours	0 hours	\$11.98
TOTAL	0.4 hours	0 hours	\$26.60



## GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #434733

**Service Request:** 434733

**Department:** Public Works

**Status:** CLOSED

**Priority:** NORMAL

**Created at:** November 14, 2017 07:30AM

**Requester:** Jose Vasquez

**Home Phone:**

**Work Phone:**

**Other Phone:**

**Created by:** josev

**Request:** PREVENTIVE MAINTENANCE. Assigned to Kevin Daxon (Siemens Tech).

**Location:** HARBOR BLVD / TRASK AVE,

**Public Property:** NO

**Square Feet:**

**Eng. Permit:**

**Police Num.:**

**Fire Num.:**

---

### Task #1

**Status:** CLOSED on November 14, 2017 08:30AM by Jose Vasquez

**Description:** No task description

**Comments:** VACUUMED CONTROLLER CABINET-REPLACED AIR FILTER-PERFORMED P.M. SCHEDULE-WALKED INTERSECTION-REMOVED GRAFFITI FROM CONTROLLER CABINET AND POLES.

**Category:** 700 SIGNAL MAINTENANCE (AUTO-

**Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES

**Requester contacted:**

**Completed by:** Jose Vasquez

**ECD:**

**Actions:** 700.26 OTHER (SEE COMMENTS), 740.1 GRAFFITI REMOVED/COVERED





# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #433047

**Service Request:** 433047

**Department:**

**Status:** CLOSED

**Priority:** NORMAL

**Created at:** October 31, 2017 01:08PM

**Requester:** Rosemarie Jacot

**Home Phone:**

**Work Phone:**

**Other Phone:**

**Created by:** rjacot

**Request:** RED SIGNAL BURN OUT LEFT TURN ARROW

**Location:** HARBOR BLVD / TRASK AVE, WB TRASK TO SB HARBOR

**Public Property:** YES

**Square Feet:**

**Eng. Permit:**

**Police Num.:**

**Fire Num.:**

**Total cost:** \$36.54

---

**Note #1 (10/31/17 by rjacot):** KEVIN 714-623-2354

---

## Task #1

**Status:** CLOSED on October 31, 2017 03:15PM by Jose Vasquez

**Description:** RED SIGNAL BURN OUT LEFT TURN ARROW

**Comments:** I arrived at the location and found that the overhead WB - SB left turn red arrow was out. I removed the old red indication and installed a new red arrow led module.

**Category:** 700 SIGNAL MAINTENANCE (AUTO- **Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES

**Requester contacted:**

**Completed by:** Jose Vasquez

**ECD:**

**Total task cost:** \$36.54

**Actions:** 700.1 REPLACED OLD LAMP WITH NEW LED MODULE

### Labor Costs

Name	Reg	OT	Total
Jose Vasquez	0.5 hours	0 hours	\$36.54
TOTAL	0.5 hours	0 hours	\$36.54



# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #432611

**Service Request:** 432611  
**Department:** Public Works  
**Status:** CLOSED  
**Priority:** NORMAL  
**Created at:** October 19, 2017 08:30AM

**Requester:** Jose Vasquez  
**Home Phone:**  
**Work Phone:**  
**Other Phone:**  
**Created by:** josev

**Request:** 2nd to last WB underpass wall-pack is out.

**Location:** HARBOR BLVD / TRASK AVE, Trask freeway underpass wall-pack lighting.

**Public Property:** NO  
**Square Feet:**

**Eng. Permit:**  
**Police Num.:**  
**Fire Num.:**

**Total cost:** \$36.54

---

## Task #1

**Status:** CLOSED on October 19, 2017 09:01AM by Jose Vasquez

**Description:** No task description

**Comments:** I installed a new lamp, but the fixture needed a new ballast. I did not have a ballast on my truck so I had Yanie pick up and install a new ballast kit from the city yard.

**Category:** 710 ST. LIGHTS/ILLUM. NAME SIGNS **Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES

**Requester contacted:**

**Completed by:** Jose Vasquez

**ECD:**

**Total task cost:** \$36.54

**Actions:** 710.1 REPLACED LAMP, 710.12 OTHER (SEE COMMENTS)

### Labor Costs

Name	Reg	OT	Total
Jose Vasquez	0.5 hours	0 hours	\$36.54
TOTAL	0.5 hours	0 hours	\$36.54



# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #428709

**Service Request:** 428709

**Department:** Public Works

**Status:** CLOSED

**Priority:** NORMAL

**Created at:** June 08, 2017 10:00AM

**Requester:** Jose Vasquez

**Home Phone:**

**Work Phone:**

**Other Phone:**

**Created by:** josev

**Request:** Safety light is out in the SB median. Assigned to Siemens contractor Yanie.

**Location:** HARBOR BLVD / TRASK AVE,

**Public Property:** NO

**Square Feet:**

**Eng. Permit:**

**Police Num.:**

**Fire Num.:**

**Total cost:** \$36.54

---

## Task #1

**Status:** CLOSED on June 08, 2017 10:30AM by Jose Vasquez

**Description:** No task description

**Category:** 710 ST. LIGHTS/ILLUM. NAME SIGNS **Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES

**Requester contacted:**

**Completed by:** Jose Vasquez

**ECD:**

**Total task cost:** \$36.54

**Actions:** 710.1 REPLACED LAMP, 710.2 REPLACED PHOTO-CELL

### Labor Costs

Name	Reg	OT	Total
Jose Vasquez	0.5 hours	0 hours	\$36.54
TOTAL	0.5 hours	0 hours	\$36.54



# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #426644

**Service Request:** 426644

**Department:** Public Works

**Status:** CLOSED

**Priority:** NORMAL

**Created at:** June 06, 2017 03:15AM

**Requester:** Jose Vasquez

**Home Phone:**

**Work Phone:**

**Other Phone:**

**Created by:** josev

**Request:** REMOVE EXISTING CM / MMU & INSTALL TESTED MONITOR.

**Location:** HARBOR BLVD / TRASK AVE,

**Public Property:** NO

**Square Feet:**

**Eng. Permit:**

**Police Num.:**

**Fire Num.:**

**Total cost:** \$7.16

---

## Task #1

**Status:** CLOSED on June 06, 2017 03:22AM by Jose Vasquez

**Description:** No task description

**Comments:** REMOVED CONFLICT MONITOR / MMU & INSTALLED TESTED MONITOR #071109647.

**Category:** 700 SIGNAL MAINTENANCE (AUTO- **Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES

**Requester contacted:**

**Completed by:** Jose Vasquez

**ECD:**

**Total task cost:** \$7.155

**Actions:** 700.26 OTHER (SEE COMMENTS)

### Labor Costs

Name	Reg	OT	Total
Jose Vasquez	0.1 hours	0 hours	\$ 7.16
TOTAL	0.1 hours	0 hours	\$ 7.16



# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #426219

**Service Request:** 426219

**Department:** Public Works

**Status:** CLOSED

**Priority:** NORMAL

**Created at:** May 30, 2017 08:30AM

**Requester:** Jose Vasquez

**Home Phone:**

**Work Phone:**

**Other Phone:**

**Created by:** josev

**Request:** "USA" DIG ALERT, MARK UNDERGROUND UTILITIES.

**Location:** HARBOR BLVD / TRASK AVE,

**Public Property:** NO

**Square Feet:**

**Eng. Permit:**

**Police Num.:**

**Fire Num.:**

**Total cost:** \$71.55

---

## Task #1

**Status:** CLOSED on May 30, 2017 09:30AM by Jose Vasquez

**Description:** No task description

**Comments:** MARKED TRAFFIC SIGNAL UNDERGROUND UTILITIES AND FIBER.

**Category:** 700 SIGNAL MAINTENANCE (AUTO- **Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES

**Requester contacted:**

**Completed by:** Jose Vasquez

**ECD:**

**Total task cost:** \$71.55

**Actions:** 700.26 OTHER (SEE COMMENTS)

### Labor Costs

Name	Reg	OT	Total
Jose Vasquez	1.0 hours	0 hours	\$71.55
TOTAL	1.0 hours	0 hours	\$71.55



# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #424949

**Service Request:** 424949

**Department:** Public Works

**Status:** CLOSED

**Priority:** NORMAL

**Created at:** May 01, 2017 11:30AM

**Requester:** Ken Vu

**Home Phone:**

**Work Phone:**

**Other Phone:**

**Created by:** josev

**Request:** Red Flex says they had a knock-down and now they have no power. Please check and advise.

**Location:** HARBOR BLVD / TRASK AVE,

**Public Property:** NO

**Square Feet:**

**Eng. Permit:**

**Police Num.:**

**Fire Num.:**

**Total cost:** \$35.77

---

## Task #1

**Status:** CLOSED on May 01, 2017 02:07PM by Jose Vasquez

**Description:** No task description

**Comments:** I found that Red Flex gets power for there equipment from our traffic signal electrical service. I found that the circuit breaker for there equipment was tripped and it was installed in the ISNS slot (wrong location). I rearranged the circuit breakers and reset their circuit. I called Ken and informed him of what I found.

**Category:** 800 MISC.

**Division:** ENGR SERVICES

**Completed by:** Jose Vasquez

**Total task cost:** \$35.775

**Actions:** 800.2 OTHER (SEE COMMENTS)

**Assigned to:** Jose Vasquez

**Requester contacted:**

**ECD:**

### Labor Costs

Name	Reg	OT	Total
Jose Vasquez	0.5 hours	0 hours	\$35.77
TOTAL	0.5 hours	0 hours	\$35.77



## GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #423772

**Service Request:** 423772

**Department:** Public Works

**Status:** CLOSED

**Priority:** NORMAL

**Created at:** April 05, 2017 01:15PM

**Requester:** Jose Vasquez

**Home Phone:**

**Work Phone:**

**Other Phone:**

**Created by:** josev

**Request:** 2 EB Frwy underpass wall pack lights are out on the south side of Trask. It's the second and forth light heading EB.

**Location:** HARBOR BLVD / TRASK AVE, EB / WB frwy underpass

**Public Property:** NO

**Square Feet:**

**Eng. Permit:**

**Police Num.:**

**Fire Num.:**

**Total cost:** \$71.55

---

### Task #1

**Status:** CLOSED on April 05, 2017 02:45PM by Jose Vasquez

**Description:** No task description

**Comments:** Replaced 2 lamps and 1 ballast.

**Category:** 710 ST. LIGHTS/ILLUM. NAME SIGNS **Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES

**Requester contacted:**

**Completed by:** Jose Vasquez

**ECD:**

**Total task cost:** \$71.55

**Actions:** 710.1 REPLACED LAMP, 710.5 INSTALLED NEW LED LIGHT FIXTURE

### Labor Costs

Name	Reg	OT	Total
Jose Vasquez	1.0 hours	0 hours	\$71.55
TOTAL	1.0 hours	0 hours	\$71.55



## GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #422974

**Service Request:** 422974

**Department:** Public Works

**Status:** CLOSED

**Priority:** NORMAL

**Created at:** March 07, 2017 12:30PM

**Requester:** Jose Vasquez

**Home Phone:**

**Work Phone:**

**Other Phone:**

**Created by:** josev

**Request:** Replace all remaining GE count-down ped modules. Assigned to Yanie (Siemens contractor).

**Location:** HARBOR BLVD / TRASK AVE,

**Public Property:** NO

**Square Feet:**

**Eng. Permit:**

**Police Num.:**

**Fire Num.:**

**Total cost:** \$71.55

---

### Task #1

**Status:** CLOSED on March 07, 2017 01:30PM by Jose Vasquez

**Description:** No task description

**Comments:** Yanie replaced 4 remaining GE ped modules with new Dialite count-down ped modules.

**Category:** 700 SIGNAL MAINTENANCE (AUTO- **Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES

**Requester contacted:**

**Completed by:** Jose Vasquez

**ECD:**

**Total task cost:** \$71.55

**Actions:** 700.15 REPLACED PEDESTRIAN MODULE

### Labor Costs

Name	Reg	OT	Total
Jose Vasquez	1.0 hours	0 hours	\$71.55
TOTAL	1.0 hours	0 hours	\$71.55





# GARDEN GROVE PUBLIC WORKS DEPARTMENT SERVICE REQUEST #422101

**Service Request:** 422101

**Department:** Police

**Status:** CLOSED

**Priority:** EMERGENCY

**Created at:** March 03, 2017 03:50PM

**Requester:** PD Dispatch

**Home Phone:**

**Work Phone:**

**Other Phone:**

**Created by:** josev

**Request:** Intersection is in 4-way red flash.

**Location:** HARBOR BLVD / TRASK AVE,

**Public Property:** NO

**Square Feet:**

**Eng. Permit:**

**Police Num.:**

**Fire Num.:**

**Total cost:** \$194.82

**File attachments:** 3

## Task #1

**Status:** CLOSED on March 03, 2017 05:15PM by Jose Vasquez

**Description:** No task description

**Comments:** Arrived at 4:20pm and found the intersection in flash. MMU indicated a conflict with phase 6 ped. I found a shorted phase 6 ped module on the SWC. I removed and discarded the old GE count down ped module and installed a new Dialite count down ped module. I reset the MMU and the intersection was operational by 4:38pm. I went ahead and removed the old phase 6 ped module on the SEC and installed a new Dialite count down ped as preventive maintenance.

**Category:** 700 SIGNAL MAINTENANCE (AUTO-

**Assigned to:** Jose Vasquez

**Division:** ENGR SERVICES

**Requester contacted:**

**Completed by:** Jose Vasquez


**ECD:**

**Total task cost:** \$194.82

**Actions:** 700.15 REPLACED PEDESTRIAN MODULE

### Labor Costs

Name	Reg	OT	Total
Jose Vasquez	0 hours	3.0 hours	\$194.82
TOTAL	0 hours	3.0 hours	\$194.82



Photos for Workorder #422101

